


Hudson Streetscapes

Peter Luizzi & Bros. Contracting, Inc.


Project start: **Mon, 7/1/2024**

Display week: **1**

TASK	PROGRESS	DAYS	START	END
General Conditions				
Precon Meeting	100%	3	6/26/24	6/30/24
Dig Safe Tickets Called In	100%	3	6/26/24	6/28/24
Dig Safe Tickets Cleared	0%	0		
Mobilization	0%	5	7/8/24	7/12/24
Tree Clearing	0%	5	7/8/24	7/12/24
2nd Street & Allen Street (Stairs)				
Demolition including Allen St Sidewalk	0%	4	7/15/24	7/18/24
Rebar Install	0%	3	7/19/24	7/23/24
Concrete Stair Install	0%	3	7/24/24	7/26/24
Railing / Site Improvements	0%	5	9/23/24	9/27/24
Warren Street & 1st Street				
Demo Curbs & Sidewalk	0%	3	7/29/24	7/31/24
Formwork & Rebar Install	0%	3	7/31/24	8/2/24
Concrete Sidewalk Install	0%	2	8/5/24	8/6/24
Curb Installation	0%	2	8/6/24	8/7/24
2nd Street & Warren Street				
Tree Removal	0%	1	7/22/24	7/22/24
Demo Curbs & Sidewalk (for widening)	0%	2	8/7/24	8/8/24
Light Pole Relocation & PB Adjustments	0%	1	8/9/24	8/9/24
Drainage Install & Removals	0%	4	8/12/24	8/15/24
Formwork & Rebar Install	0%	2	8/14/24	8/15/24
Concrete Sidewalk Install & Paver Install	0%	2	8/19/24	8/20/24
Granite Curb & Setts Install	0%	2	8/21/24	8/22/24
Landscape Bedding	0%	2	9/30/24	10/1/24

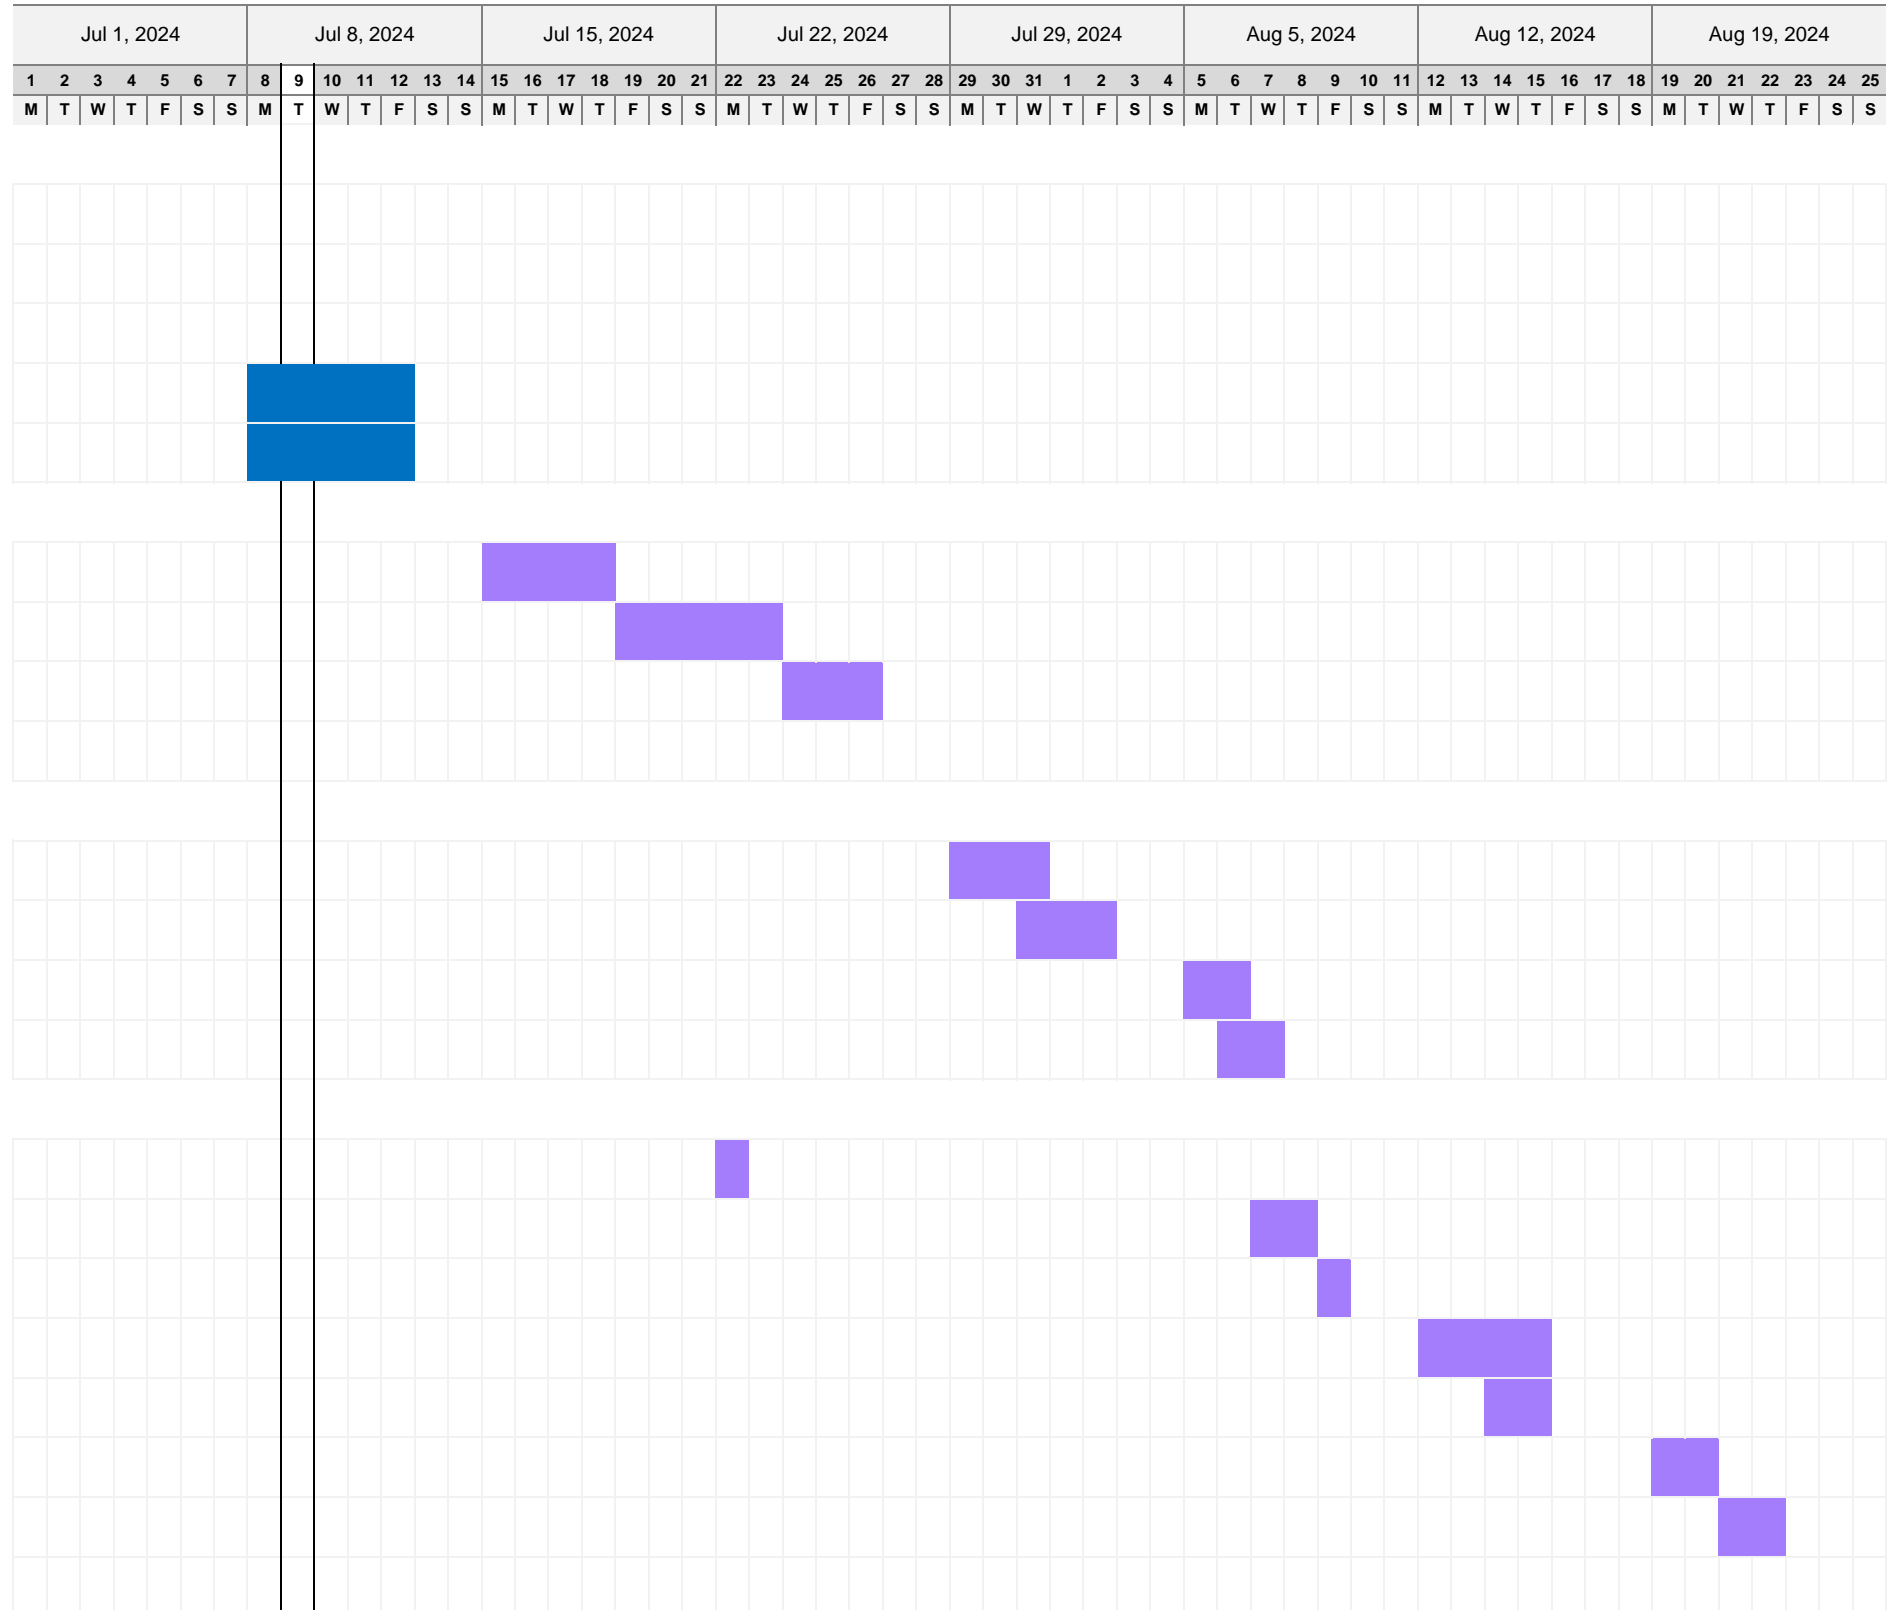

TASK	PROGRESS	DAYS	START	END
Pedestrian Improvements	0%	2	9/30/24	10/1/24
Mill & Pave Roadway	0%	5	9/30/24	10/4/24
Front Street & State Street				
Tree Removal	0%	1	7/23/24	7/23/24
Demo Curbs & Sidewalk (for widening)	0%	2	8/19/24	8/20/24
Light Pole Relocation & PB Adjustments	0%	1	8/21/24	8/21/24
Drainage Install & Removals	0%	3	8/21/24	8/23/24
Formwork & Rebar Install	0%	2	8/26/24	8/27/24
Concrete Sidewalk Install & Paver Install	0%	2	8/28/24	8/29/24
Granite Curb & Setts Install	0%	2	8/28/24	8/29/24
Landscape Bedding	0%	2	10/2/24	10/3/24
Pedestrian Improvements	0%	2	10/2/24	10/3/24
Front Street & Columbia Street				
Tree Removal	0%	1	7/24/24	7/24/24
Demo Curbs & Sidewalk (for widening)	0%	2	8/26/24	8/27/24
Light Pole Relocation & PB Adjustments	0%	1	8/28/24	8/28/24
Drainage Install & Removals	0%	3	8/28/24	8/30/24
Formwork & Rebar Install	0%	3	9/2/24	9/4/24
Concrete Sidewalk Install & Paver Install	0%	2	9/5/24	9/6/24
Granite Curb & Setts Install	0%	2	9/5/24	9/6/24
Landscape Bedding	0%	2	10/4/24	10/7/24
Pedestrian Improvements	0%	2	10/4/24	10/7/24
Front Street & Prison Alley				
Tree Removal	0%	1	7/25/24	7/25/24
Demo Curbs & Sidewalk (for widening)	0%	2	9/2/24	9/3/24
Light Pole Relocation & PB Adjustments	0%	1	9/4/24	9/4/24
Drainage Install & Removals	0%	3	9/4/24	9/6/24
Formwork & Rebar Install	0%	3	9/9/24	9/11/24
Concrete Sidewalk Install & Paver Install	0%	2	9/12/24	9/13/24
Granite Curb & Setts Install	0%	2	9/12/24	9/13/24

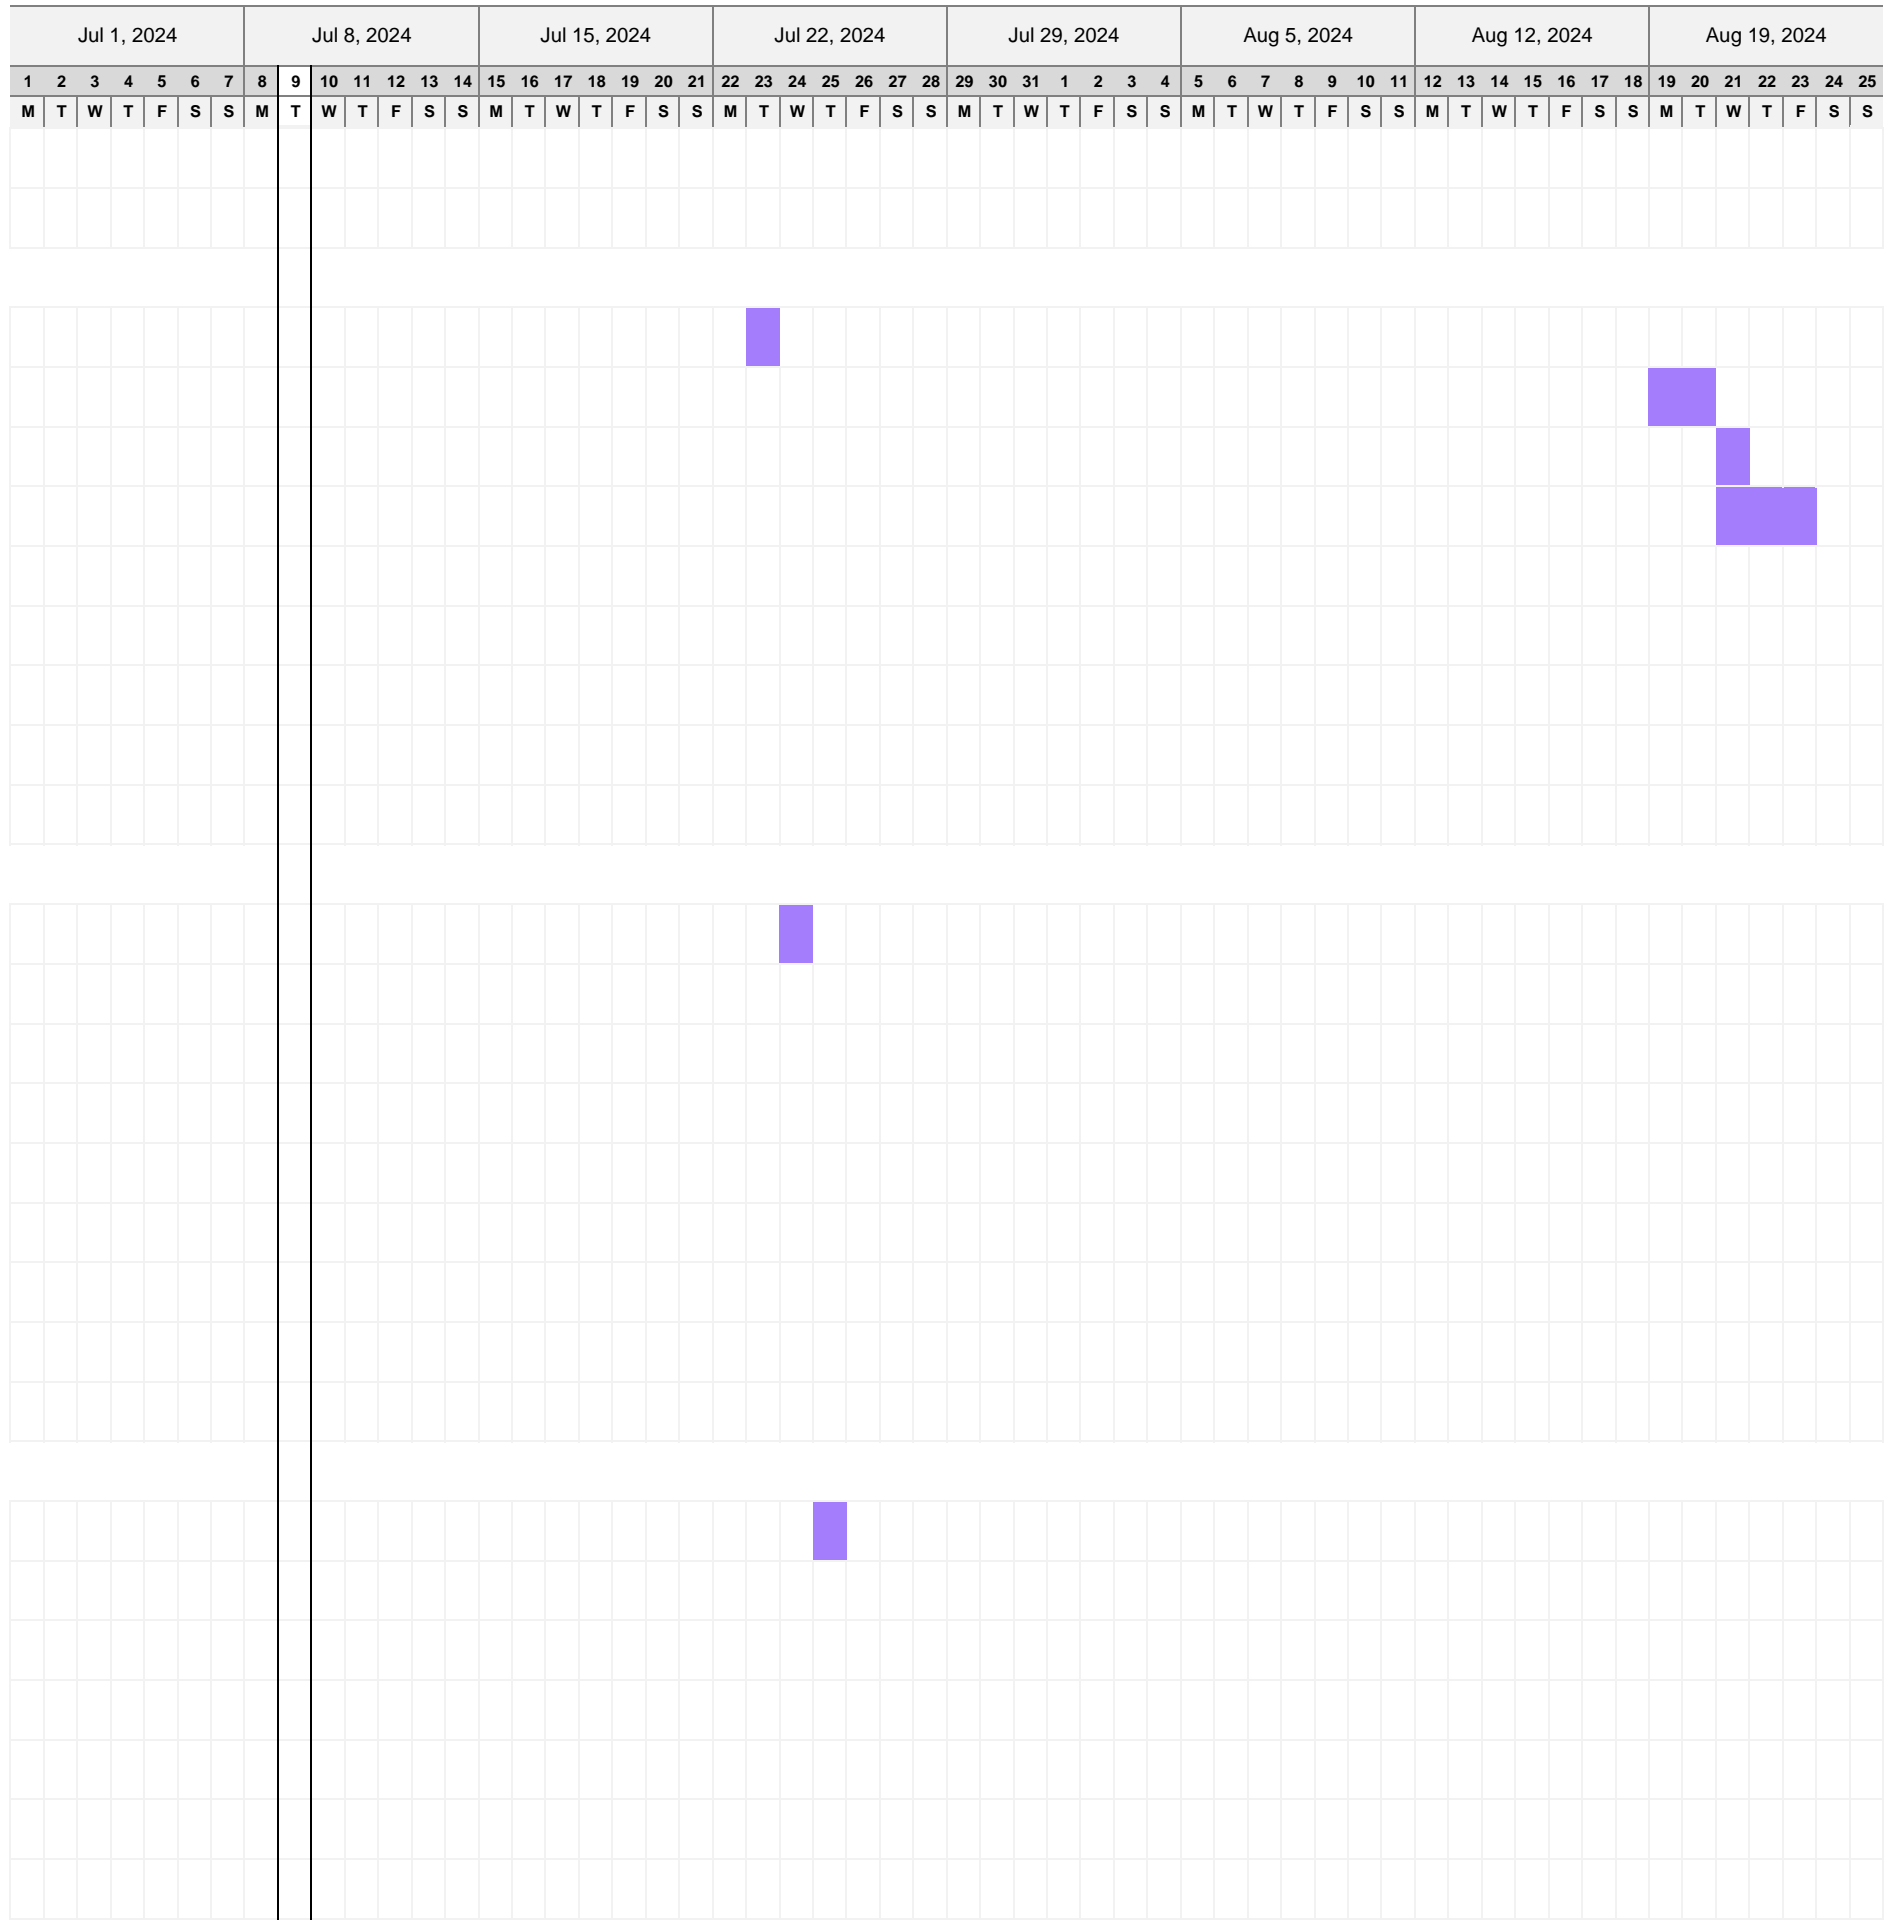

TASK	PROGRESS	DAYS	START	END
Landscape Bedding	0%	2	10/8/24	10/9/24
Pedestrian Improvements	0%	2	10/8/24	10/9/24
Front Street & Warren Street				
Tree Removal	0%	1	7/26/24	7/26/24
Demo Curbs & Sidewalk (for widening)	0%	2	9/9/24	9/10/24
Light Pole Relocation & PB Adjustments	0%	1	9/11/24	9/11/24
Drainage Install & Removals	0%	3	9/11/24	9/13/24
Formwork & Rebar Install	0%	3	9/16/24	9/18/24
Concrete Sidewalk Install & Paver Install	0%	2	9/19/24	9/20/24
Granite Curb & Setts Install	0%	2	9/19/24	9/20/24
Landscape Bedding	0%	2	10/10/24	10/11/24
Pedestrian Improvements	0%	2	10/10/24	10/11/24
Mill & Pave Roadway	0%	5	9/30/24	10/4/24
Front Street Btwn Warren St and Cross Street				
Tree Removal	0%	3	7/29/24	7/31/24
Demo Curbs & Sidewalk (for widening)	0%	2	9/16/24	9/17/24
Light Pole Relocation & PB Adjustments	0%	1	9/18/24	9/18/24
Drainage Install & Removals	0%	3	9/18/24	9/20/24
Formwork & Rebar Install	0%	3	9/23/24	9/25/24
Concrete Sidewalk Install & Paver Install	0%	2	9/26/24	9/27/24
Granite Curb & Setts Install	0%	1	9/27/24	9/28/24
Landscape Bedding	0%	2	10/14/24	10/15/24
Pedestrian Improvements	0%	2	10/14/24	10/15/24
Mill & Pave Roadway	0%	5	9/30/24	10/4/24

Jul 1, 2024								Jul 8, 2024							Jul 15, 2024							Jul 22, 2024							Jul 29, 2024							Aug 5, 2024							Aug 12, 2024							Aug 19, 2024																										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25																					
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S														
